

Monument Square Roundabout Improvement

PID 103793

Public Open House Meetings

Tuesday, April 30, 2019 at 3:00 PM and 7:00 PM

City of Urbana Municipal Building | 205 South Main Street

2nd Floor Training Room

The environmental review, consultation and other actions required by applicable Federal environmental laws for this project are being, or have been, carried out by ODOT pursuant to 23 U.S.C. 327 and a Memorandum of Understanding dated 12/11/2015, and executed by FHWA and ODOT.

Project Construction Update

The City anticipates that construction will begin on **Monday, May 6, 2019** and last throughout the summer, ending in the resurfacing of the entire downtown (Monument Square and one block in each direction). The final completion date is October 31, 2019. Please periodically check the City of Urbana website (www.urbanaohio.com) and Facebook page for project updates.

Businesses can remain open as normal. Parking will be affected but pedestrian access will be maintained.

How will it affect me?

Street Closures – Closures are planned to occur individually over the course of 6 separate construction phases.

Phases	Estimated Duration	Traffic Impact	Parking Restriction
Phase 1 Roundabout Truck Apron Construction	May 6 – May 19	Traffic maintained	One quadrant of the Square closed to parking.
Phase 2 North Leg Installation	May 20 – Jun 24	100 block of N. Main St. closure (Monument Sq. to Court St.)	100 block of N. Main St. and up to two quadrants of the Square closed to parking.
Phase 3 East Leg Installation	Jun 25 – Aug 4	100 block of Scioto St. closure (Monument Sq. to Locust St.)	100 block of Scioto St. and up to two quadrants of the Square closed to parking.
Phase 4 South Leg Installation	Aug 5 – Sep 11	100 block of S. Main St. closure (Monument Sq. to Market St.)	100 block of S. Main St. and up to two quadrants of the Square closed to parking.
Phase 5 West Leg Installation	Sep 12 – Oct 20	100 block of Miami St. closure (Monument Sq. to Walnut St.)	100 block of Miami St. and up to two quadrants of the Square closed to parking.
Phase 6 Final Project Milling and Paving (overnight)	Oct 21 – Oct 31	Traffic maintained	Parking restricted during the paving and milling operations.

Remember to look for notice of closure signs and detours (see reverse) during the construction.

Driveway Impacts

Driveway access, for instance to parking lots or alleyways, will be maintained through the closed leg from one end or the other. The contractor will be replacing almost all parking lot or alleyway concrete approaches. This will cause an inconvenience of about 7 days.

Pedestrian Accessibility

Pedestrian access to downtown businesses will be maintained throughout the duration of the project. Concrete sidewalk work may take place near your entryway, so please work with the contractor so that they can make reasonable accommodations.

Questions or Comments? Contact Us!

True Inspection Services, LLC

Ron Quesenberry – Project Manager

Phone: (937) 681 - 9000

Email: Ron.Quesenberry@trueinspectionsservices.com



R. B. JERGENS


TTIS
TRUE INSPECTION SERVICES, LLC



The completed roundabout will feature similar pedestrian crossings.


Phase 2 Detour: May 20 – June 24

Street Closure from Monument Square to Court Street

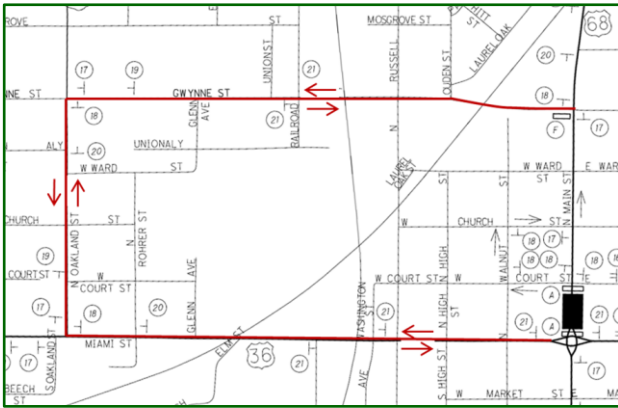


Phase 3 Detour: June 25 – August 4

Street Closure from Monument Square to Locust Street

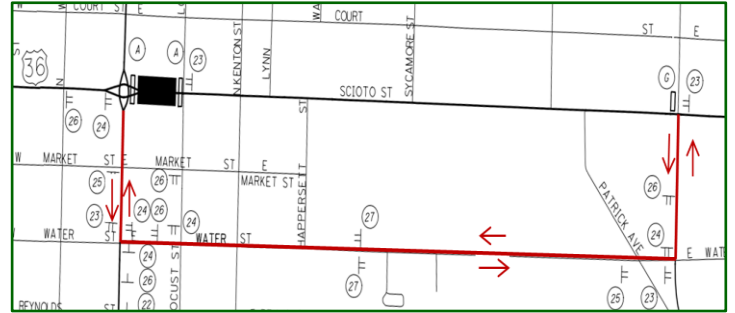

Phase 4 Detour: August 5 – September 11

Street Closure from Monument Square to Market Street

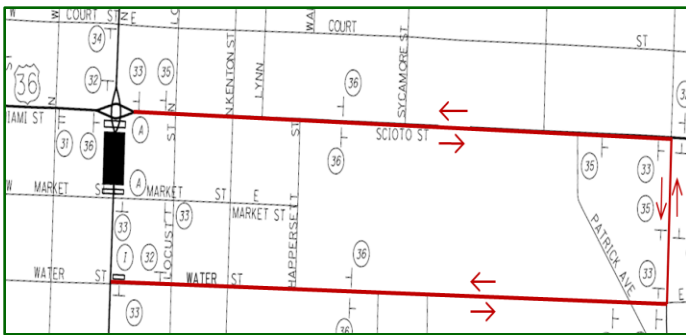

Phase 5 Detour: September 12 – October 20

Street Closure from Monument Square to Walnut Street



Concept drawing of the completed improvements
